


Adams Street - Project Schedule - 10.25.23

ID	Task Name	Duration	Start	Finish	Predecessors	Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024	
						Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	
1	Adams Street Water & Sewer - Utility Upgrades	315 days	Mon 7/31/23	Sun 6/9/24															19%
5	Preconstruction Activities	44 days	Mon 7/31/23	Fri 9/29/23															100%
7	Prepare, Submit, and Approve Submittals	25 days	Mon 7/31/23	Fri 9/1/23															100%
6	Survey Sewer Lines	5 days	Mon 8/14/23	Fri 8/18/23															100%
8	Manhole Order and Delivery	15 days	Mon 9/11/23	Fri 9/29/23	7														100%
2	Contract Dates	301 days	Mon 8/14/23	Sun 6/9/24															0%
3	Notice to Proceed	1 day	Mon 8/14/23	Mon 8/14/23															0%
4	Substantial Completion	1 day	Sun 6/9/24	Sun 6/9/24															0%
42	Sewer Line B - 8" PVC - 2,030LF	125 days	Mon 10/2/23	Thu 4/4/24															18%
62	Sawcut/ Pothole	3 days	Mon 10/2/23	Wed 10/4/23															100%
63	Install MH B9	2 days	Mon 10/9/23	Tue 10/10/23	8,31														100%
61	MH 9 20+30.17 to MH 8 18+46.11 with 4 services; (1 service remaining)	13 days	Wed 10/11/23	Fri 10/27/23	63														80%
60	Install MH B8	1 day	Tue 10/17/23	Tue 10/17/23															100%
59	MH B8 18+46.11 to MH B7 14+97.69 with 10 service	18 days	Wed 10/18/23	Fri 11/10/23	60														50%
57	Install MH B7	1 day	Thu 10/26/23	Thu 10/26/23															0%
56	MH B7 14+97.69 to MH B6 11+69.07 to with 8 servic	17 days	Fri 10/27/23	Mon 11/20/23	57														0%
53	Install MH B6	1 day	Tue 11/21/23	Tue 11/21/23	56														0%
55	Lay Connect 20 LF to MH B6 to Stewart Street	1 day	Wed 11/22/23	Wed 11/22/23	53														0%
54	Lay/Connect 23 LF from MH B6 to MH B11	1 day	Mon 11/27/23	Mon 11/27/23	55														0%
52	MH B6 11+69.07 to MH B5 8+44.86 with 7 services	18 days	Tue 11/28/23	Thu 12/21/23	54														0%
50	Install MH B5 and lay/connect 20 LF Jennings Street	3 days	Tue 1/2/24	Thu 1/4/24	52														0%
51	Remove/Replace 30" CMP with pipe support	4 days	Fri 1/5/24	Wed 1/10/24	50														0%
49	MH B 5 8+44.86 to MH B4 6+77.97 with 4 services	11 days	Thu 1/11/24	Thu 1/25/24	51														0%
48	Install MH B4 and lay/connect 20 LF Adams Court	2 days	Fri 1/26/24	Mon 1/29/24	49														0%
47	MH B4 6+77.97 to MH B3 5+46.61 to with 1 service	5 days	Tue 1/30/24	Mon 2/5/24	48														0%
46	Install MH B3	1 day	Tue 2/6/24	Tue 2/6/24	47														0%
45	MH B3 5+46.61 to 2+48.95 MH B2 with 6 services	16 days	Wed 2/7/24	Wed 2/28/24	46														0%
44	Install MH B2	1 day	Thu 2/29/24	Thu 2/29/24	45														0%
43	MH B2 2+48.95 to MH B1 0+00, install 5 services	19 days	Fri 3/1/24	Wed 3/27/24	44														0%
64	Install B1 0+00	1 day	Thu 3/28/24	Thu 3/28/24	43														0%
58	Testing Sewer Line B	5 days	Fri 3/29/24	Thu 4/4/24	64														0%
9	Water Line - 8" DIP	83 days	Tue 1/2/24	Thu 4/25/24															0%
10	Sawcut/ Pothole	5 days	Tue 1/2/24	Mon 1/8/24															0%
11	Lay Sta. 0+00 to 2+24	4 days	Tue 1/9/24	Fri 1/12/24	10														0%
12	Install Fire Hydrant 2+24	1 day	Mon 1/15/24	Mon 1/15/24	11														0%
28	Excavate and Install Services	60 days	Mon 1/15/24	Fri 4/5/24	11														0%

Critical		Split		Finish-only		Baseline Milestone		Manual Summary		Inactive Task	
Critical Split		Task Progress		Duration-only		Milestone		Project Summary		Inactive Milestone	
Critical Progress		Manual Task		Baseline		Summary Progress		External Tasks		Inactive Summary	
Task		Start-only		Baseline Split		Summary		External Milestone		Deadline	

Adams Street - Project Schedule - 10.25.23

ID	Task Name	Duration	Start	Finish	Predecessors	Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024
						Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
13	Lay Sta. 2+24 to 6+20	5 days	Tue 1/16/24	Mon 1/22/24	12													
14	Air Release Valve Assembly 6+20	1 day	Tue 1/23/24	Tue 1/23/24	13													
15	Lay Sta. 6+20 to 7+63	2 days	Wed 1/24/24	Thu 1/25/24	14													
16	Install Fire Hydrant 7+63	1 day	Fri 1/26/24	Fri 1/26/24	15													
17	Lay Sta. 7+63 to 18+87	15 days	Mon 1/29/24	Fri 2/16/24	16													
18	Install Fire Hydrant 18+87	1 day	Mon 2/19/24	Mon 2/19/24	17													
19	Lay Sta. 18+87 to 19+90	2 days	Tue 2/20/24	Wed 2/21/24	18													
20	Air Release Valve Assembly 19+90	1 day	Thu 2/22/24	Thu 2/22/24	19													
21	Lay Sta. 19+90 to 22+26	5 days	Fri 2/23/24	Thu 2/29/24	20													
22	Install Fire Hydrant 22+26	1 day	Fri 3/1/24	Fri 3/1/24	21													
23	Lay Sta. 22+26 to 26+16	6 days	Mon 3/4/24	Mon 3/11/24	22													
24	Install Fire Hydrant 26+16	1 day	Tue 3/12/24	Tue 3/12/24	23													
25	Lay Sta. 26+16 to 27+33	2 days	Wed 3/13/24	Thu 3/14/24	24													
26	Testing/Disinfection/ Prep Tie-In	10 days	Fri 3/15/24	Thu 3/28/24	25													
27	Tie-In to Existing and Cut and Cap	15 days	Fri 3/29/24	Thu 4/18/24	26													
29	Demo - Remove old hydrants, valve boxes, meters	5 days	Fri 4/19/24	Thu 4/25/24	27													
30	Sewer Line A - 8" PVC - 653LF	167 days	Thu 10/5/23	Fri 6/7/24														
31	Saw Cut/ Pothole	2 days	Thu 10/5/23	Fri 10/6/23	62													
32	Sta. 0+00 @ Carolyn Avenue to 0+20 MH A6	3 days	Tue 4/9/24	Thu 4/11/24														
33	Sta. 0+00 MHA6 to MH A4 with 4 services	10 days	Fri 4/12/24	Thu 4/25/24	32													
34	Install MH A4	1 day	Fri 4/26/24	Fri 4/26/24	33													
35	MH A4 2+09.2 to 3+38.56 MH A3 with 2 services	6 days	Mon 4/29/24	Mon 5/6/24	34													
36	Install MH A3 and lay/connect 20 LF Generals Retreat	2 days	Tue 5/7/24	Wed 5/8/24	35													
37	MH A3 Sta. 3+38.56 to MH A2 4+57.38 with 2 services	5 days	Thu 5/9/24	Wed 5/15/24	36													
38	Install MH A2	1 day	Thu 5/16/24	Thu 5/16/24	37													
39	MH A2 4+57.38 to MH A1 6+63.32 with 4 services	9 days	Fri 5/17/24	Thu 5/30/24	38													
40	Install MH A1	1 day	Fri 5/31/24	Fri 5/31/24	39													
41	Testing Sewer Line A	5 days	Mon 6/3/24	Fri 6/7/24	40													

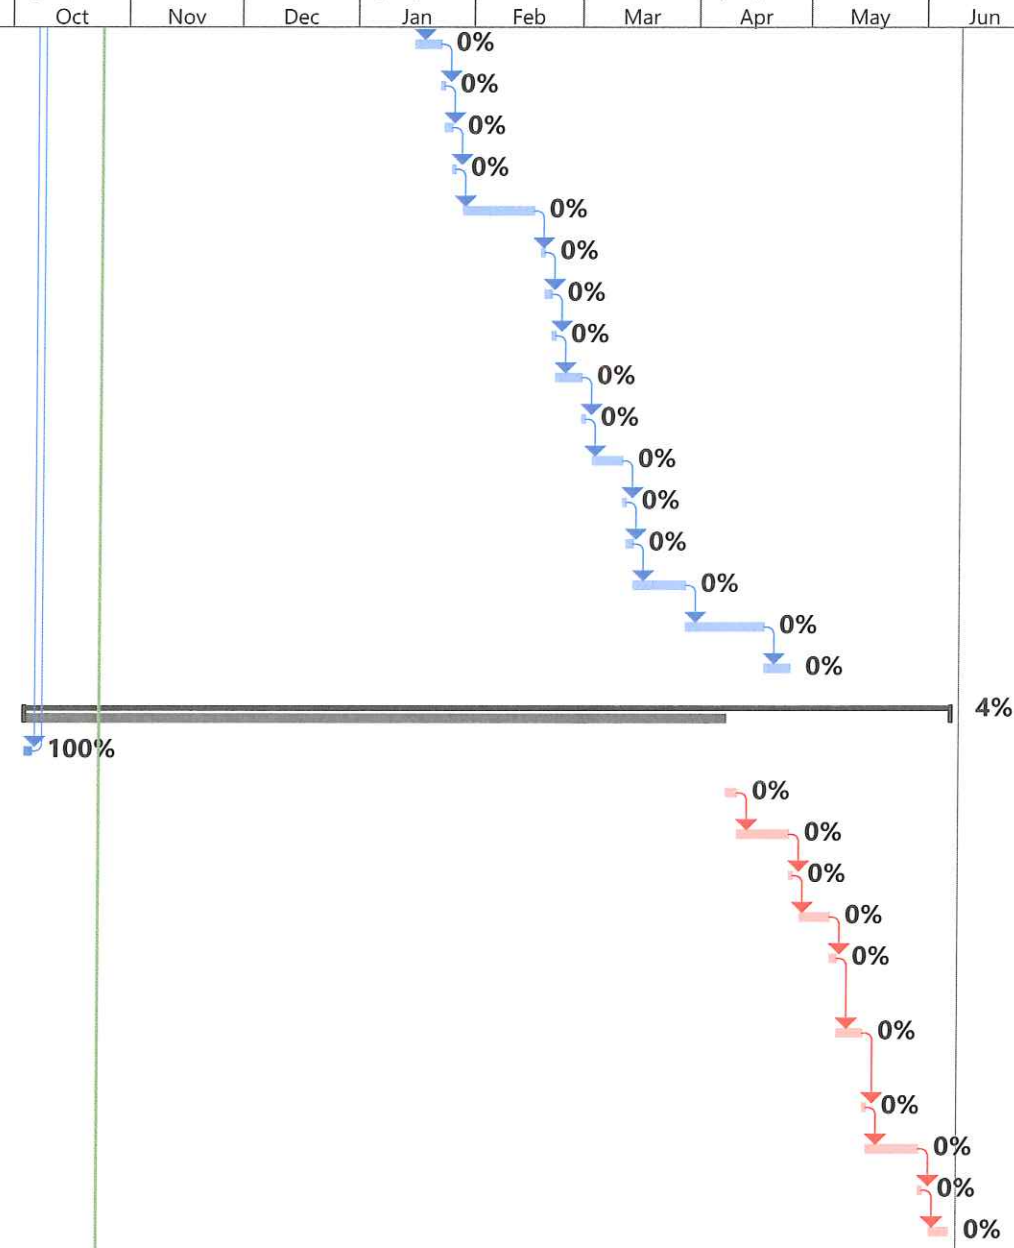

Critical		Split		Finish-only		Baseline Milestone		Manual Summary		Inactive Task	
Critical Split		Task Progress		Duration-only		Milestone		Project Summary		Inactive Milestone	
Critical Progress		Manual Task		Baseline		Summary Progress		External Tasks		Inactive Summary	
Task		Start-only		Baseline Split		Summary		External Milestone		Deadline	
